


**Muskrat Falls Project
Oversight Committee
August Reporting
October 7, 2020**

August 2020 Project Progress

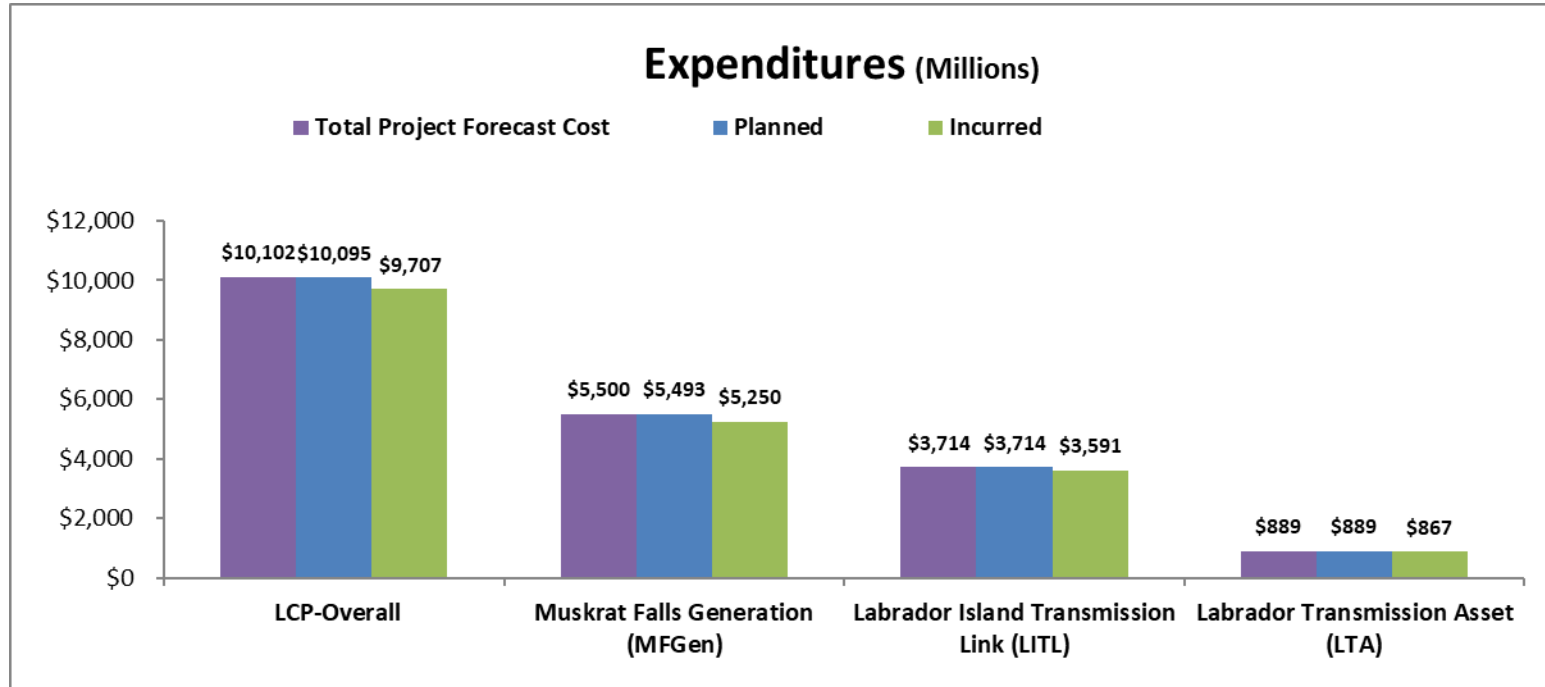

Project Costs

Muskrat Falls Project Costs at August 2020 (\$000's)

Muskrat Falls Project: Sub-Project	Percentage of Total Budget	Project Budget at June 2017 (LTA and LITL Contingency amended in March 2018 and LTA Contingency amended November 2019)	Planned Costs as of August 2020	Incurred Costs as of August 2020	Percentage of Budget Incurred	Variance Planned vs. Incurred Costs	Variance as % of Planned Costs	Project Forecast Cost
Muskrat Falls Generating Facility	54.4%	\$5,500,056	\$5,492,573	\$5,249,530	95.4%	(\$243,043)	-4.4%	\$5,500,056
Labrador-Island Transmission Link	36.8%	\$3,713,716	\$3,713,716	\$3,590,906	96.7%	(\$122,810)	-3.3%	\$3,713,716
Labrador Transmission Assets	8.8%	\$888,556	\$888,556	\$867,012	97.6%	(\$21,544)	-2.4%	\$888,556
Total	100.0%	\$10,102,328	\$10,094,845	\$9,707,448	96.1%	(\$387,397)	-3.8%	\$10,102,328

Overall Final Forecast Cost unchanged from June 2017 AFE. Additional Risks (\$850 million) not included.

Contingency Allocation

Contingency Budget at August 2020 (\$ 000's)

	Project Budget June 2017 and amended March 2018 and November 2019	Project Forecast Cost July 2020	Project Forecast Cost August 2020	Change from Previous Period	Variance PFC from Budget
Muskrat Falls					
Total Project	\$324,162	\$101,473	\$101,473	\$0	(\$222,689)
